





Microsoft Project Online 소개 및 제안

아이티퓨처스
대표컨설턴트 정수현
james@itfutures.co.kr
010-4545-6822

Microsoft Project Soution 역할 모델


<p>(Portfolio Manager , CIO)</p>  <ul style="list-style-type: none"> 전체 프로젝트 현황 모니터링 Project Portfolio Management Dashboard Monitoring
<p>PMO</p>  <ul style="list-style-type: none"> 전체 프로젝트 변경관리 전체 프로젝트 진행관리 Project Workflow Approval
<p>PM</p>  <ul style="list-style-type: none"> 프로젝트 등록 세부작업(Task) 등록 자원할당 일정관리 산출물 관리 이슈,리스크,보고서 관리
<p>Team Member</p>  <ul style="list-style-type: none"> 내 작업 확인 및 진행률 등록 이슈 등록 리스크 등록

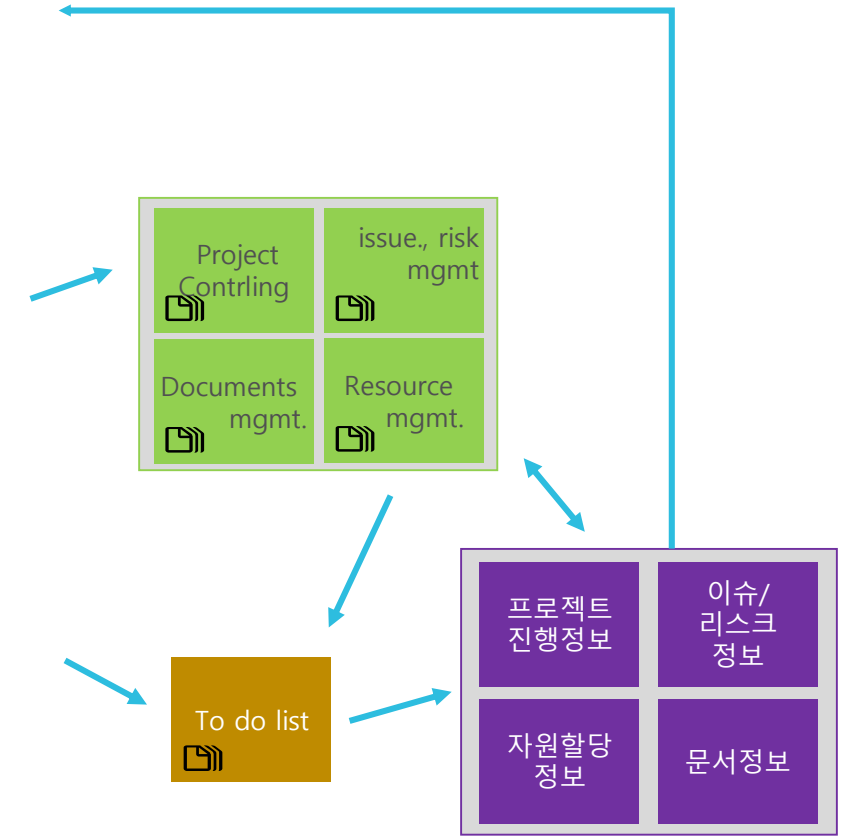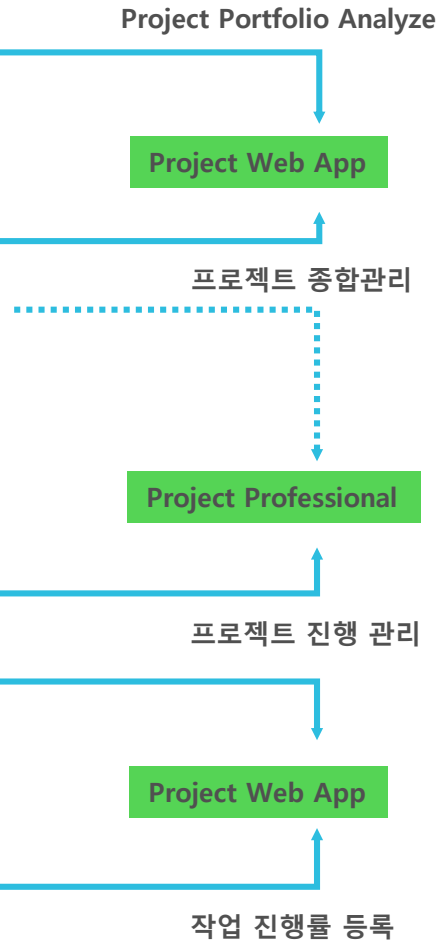

Project

Project Solution 구축 CASE 0 – MS Project 사용

- MS Project 를 이용하여 Stand Alone 한 환경으로 사용
- 사용자의 요구사항이 개인(PM) 이 소규모의 단일 프로젝트를 관리하고자 하는 개인이나 부서단위 기업에 권장
- 구매 즉시 사용 가능

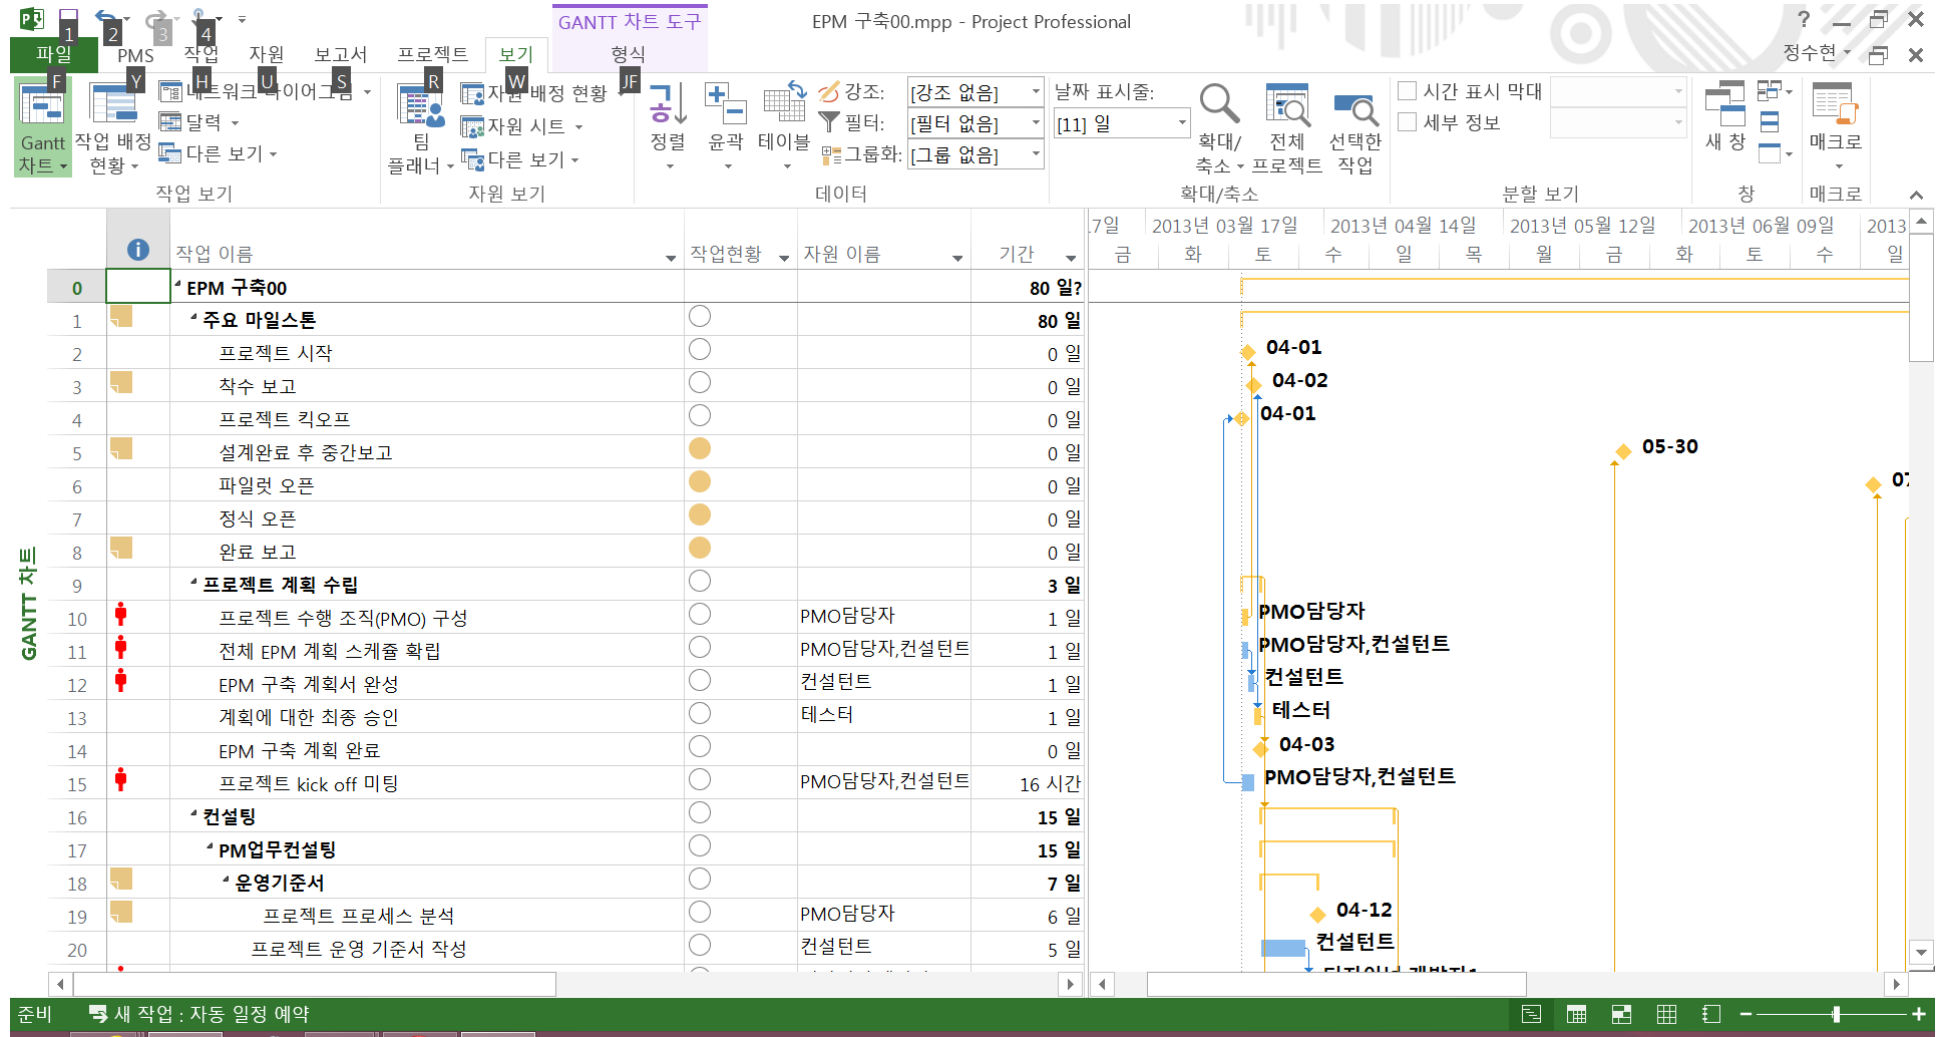

Project Solution 구축 CASE 1 – On Premise 설치형

- 커스터마이징 없이 기본적인 Project Server 솔루션의 기능을 이용하여 구축.
- 사용자의 요구사항이 주로 일정관리에 초점을 맞추고 있으며, 우선적으로 사용 후 향후 확장을 고려하는 기업에 권장
- 설치 후 셋팅, 즉시 사용가능

The screenshot displays the Project Web App interface for '프로젝트 센터' (Project Center). The main area features a Gantt chart titled 'Health Assessment Reporting Tool' with a timeline from 2012 to 2014. Projects are represented by colored bars indicating their duration and status. Below the chart is a table listing various projects with their start and end dates, completion percentages, and work hours.

프로젝트 이름	시작	마침	완료율	작업
Acquisition Target Analysis	2013-11-28	2014-09-12	0%	2,728h
Apparel ERP Upgrade	2013-01-28	2013-08-30	0%	2,590h
Audit Tracking Solution	2013-01-21	2013-07-30	0%	1,891h
Automated Software Installation	2013-02-18	2013-06-05	0%	824h
Biothermal ear heating system for helmets	2012-01-16	2014-02-05	0%	120h
Catalog Publishing	2013-01-30	2014-01-30	0%	3,496h
CFO Campaign	2012-06-25	2013-09-13	0%	6,808h
Construction safety equipment	2013-03-04	2015-03-12	0%	8,040h
Content Filtering Design and Implementation	2012-02-20	2012-12-14	0%	0h

Project

Project Solution 구축 CASE 2 – Project Online

- 구독의 개념으로 1년단위로 가입.
- 구독 즉시 사용할 수 있는 장점
- 사용자의 요구사항이 주로 일정관리에 초점을 맞추고 있으며, 별도의 전산관리 인프라에 대한 자원이 적은 기업에 권장
- 일반적인 구축 기간은 한달이내에 완료

Office 365 뉴스피드 SkyDrive 사이트 프로젝트 ... 관리자 Jeong James

찾아보기 공유 팔로우

아이티뷰처스 Project Online

현재 사이트 검색

Project Web App 시작 이 항목 제거

프로젝트를 만들거나 가져오세요. 보고서를 통해 이해를 넓히세요. 사이트 공유 그 밖의 기능 나만의 브랜드 설정 목록, 라이브러리 등 다양한 앱 추가


작업 추적

프로젝트 승인: 미정 0개 작업: 새 작업 5개 보고서

프로젝트 승인 작업 작업표 문제점 및 위험 자원 상황 보고서 대시보드 보고서 서버 설정 링크 편집

Project Online Dashboard (Power BI)


- Project Online 은 Project Server 와는 다르게 클라우드 서비스 이기 때문에 커스터마이징이 어려움
- Native 기능으로 사용하는 것을 원칙으로 하되, 대시보드 의 경우는 Power BI 를 이용하여 구성할 수 있음

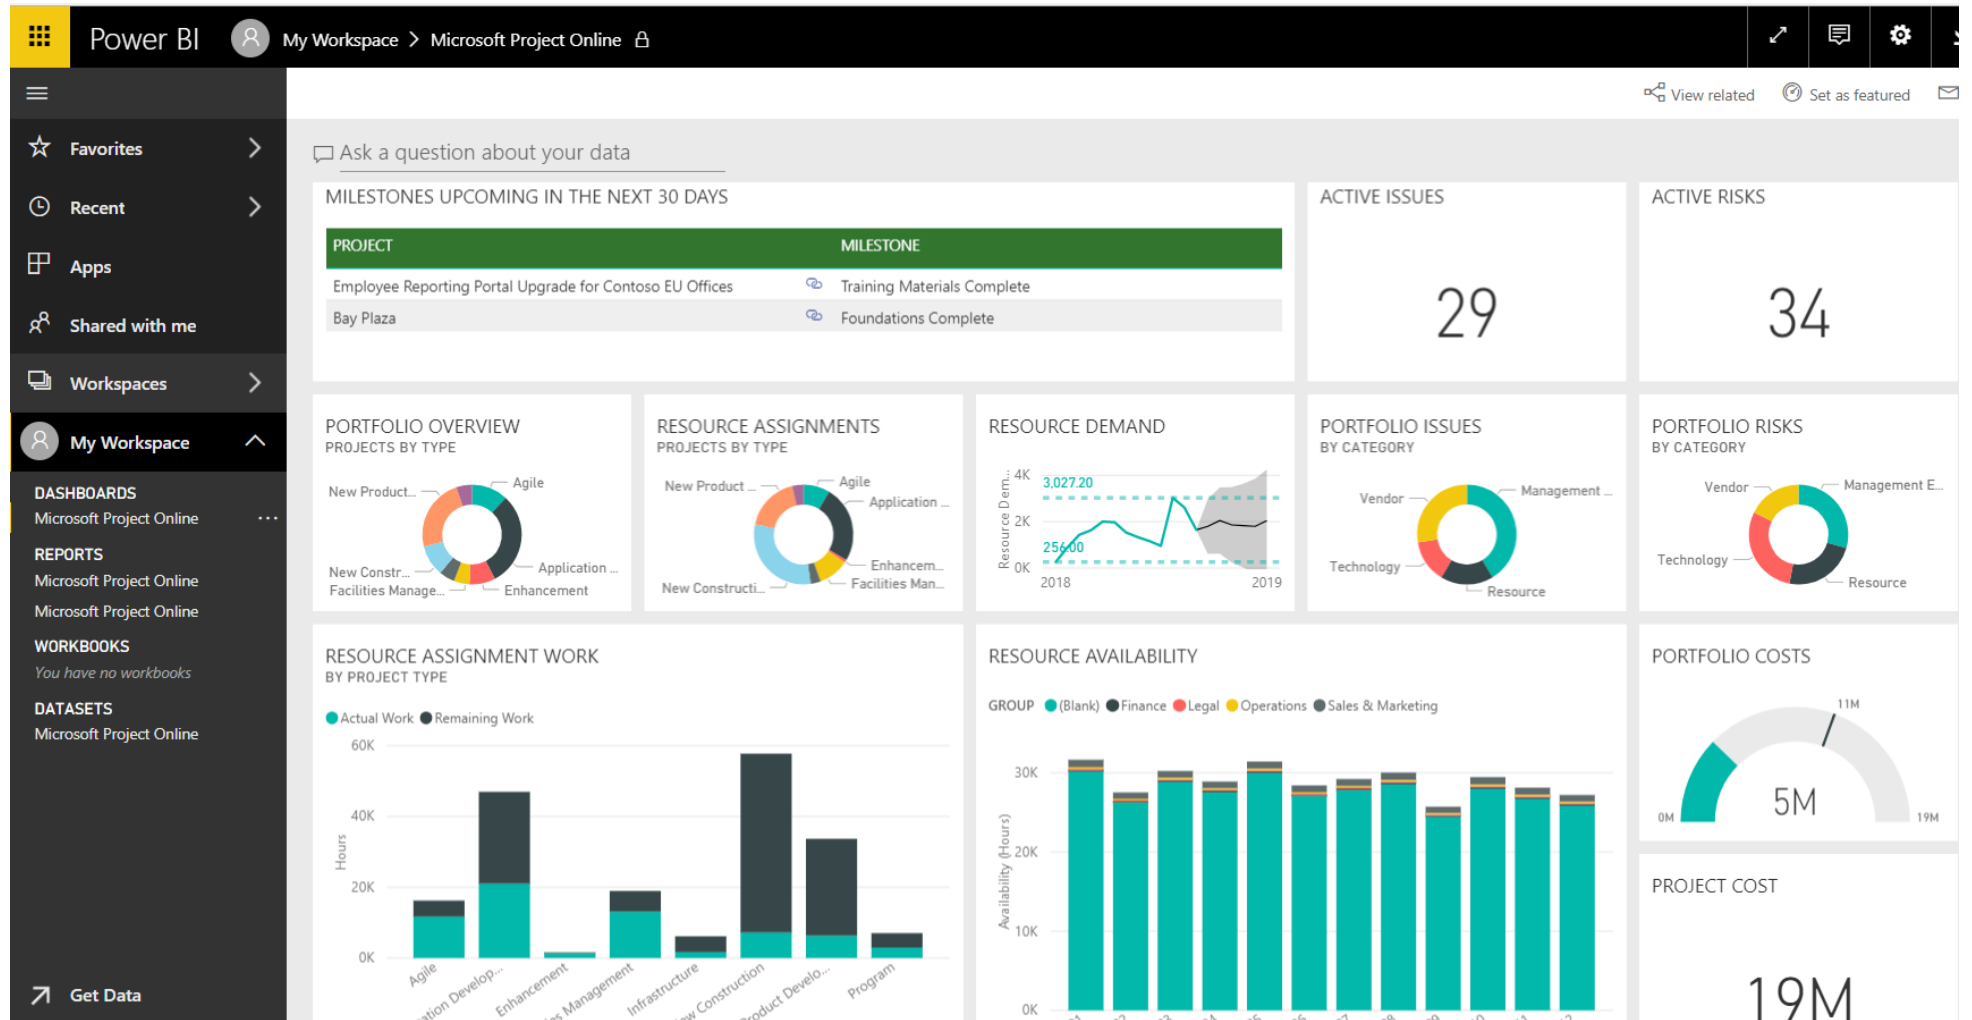

Project

Project Solution Built-in Function (Project Server, Online)

- Project Online 과 Project Server 의 기본 기능은 거의 같습니다.
- 단지, 설치형과 클라우드 서비스의 차이가 있습니다.

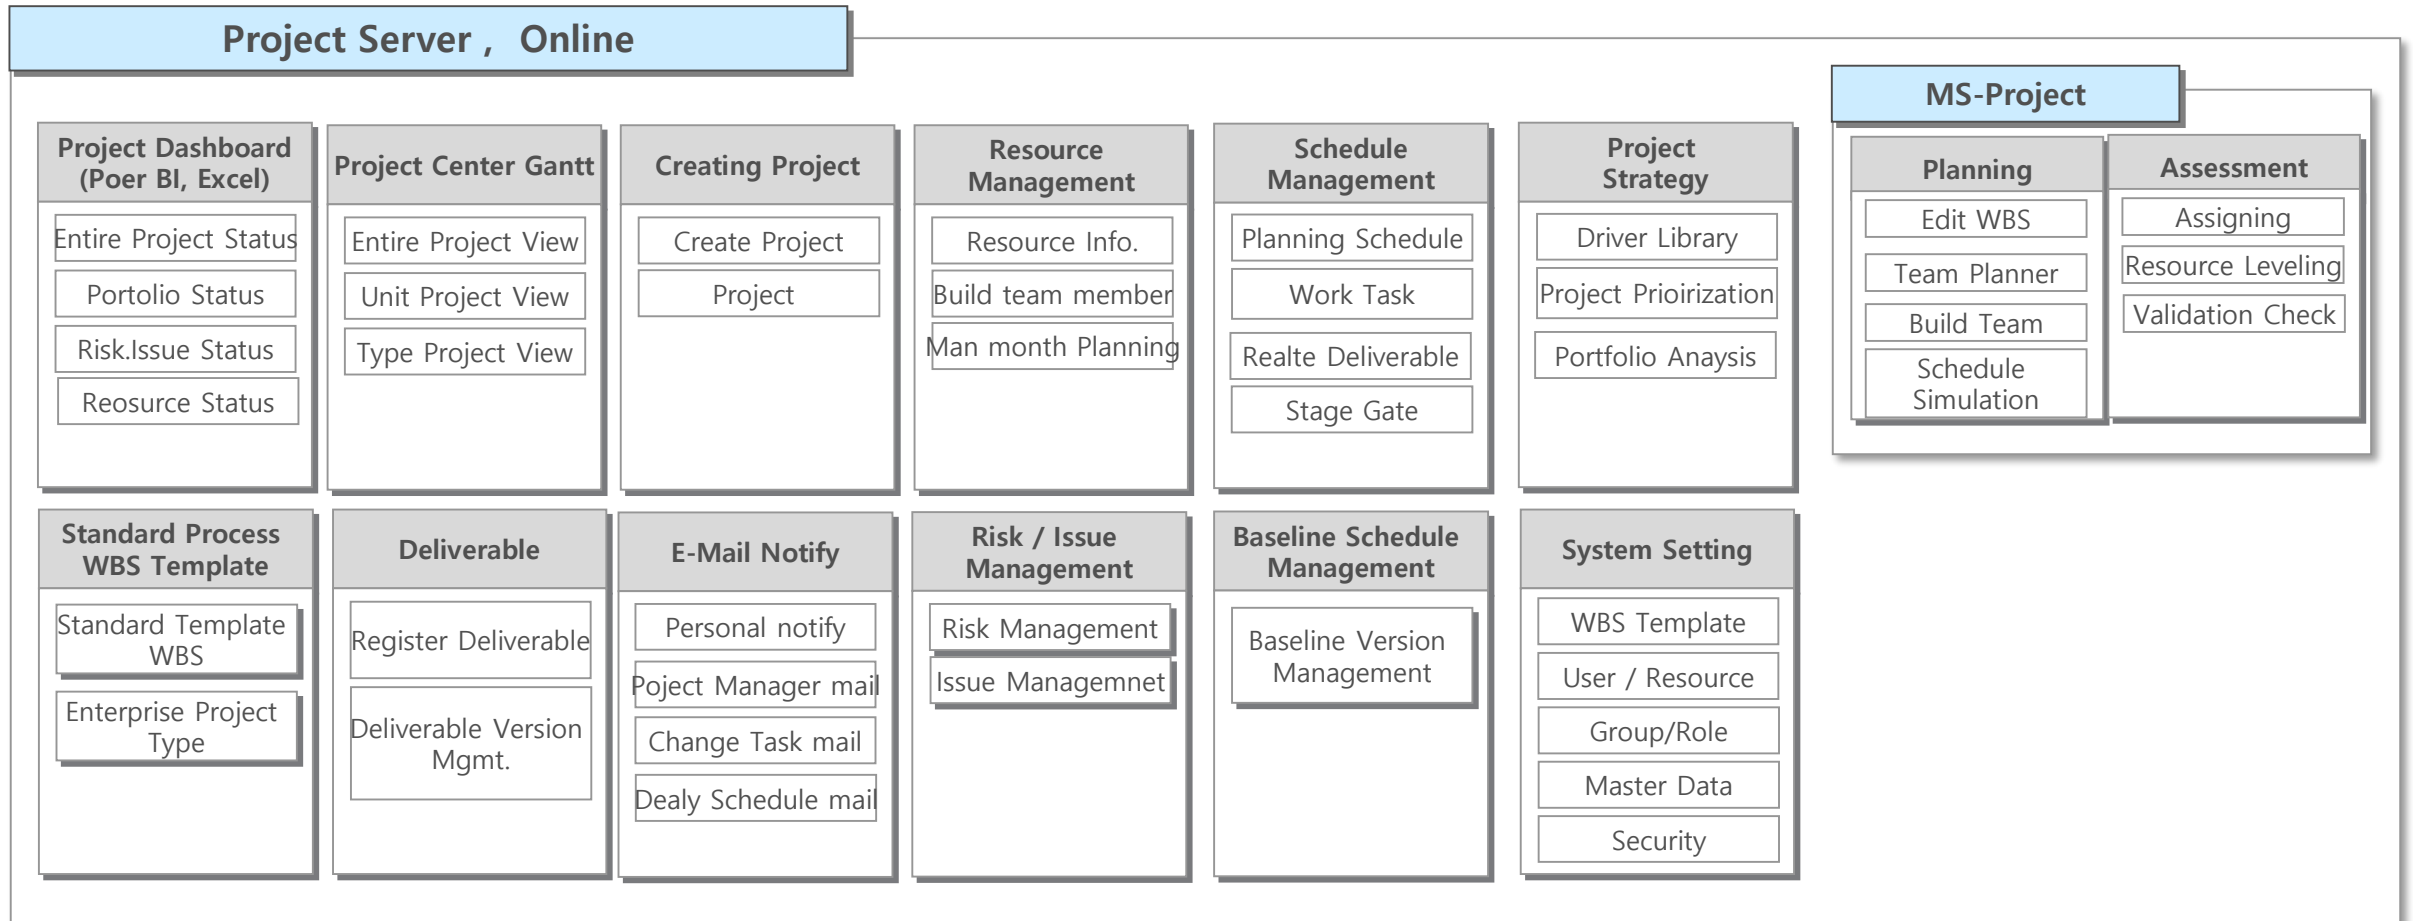

Project Online Overview

Project Online Introduction

Microsoft Project Online

- Project Online 을 이용하기 위해서는 최소한 하나 이상의 P3 PLAN 구독이 필요합니다.
- 그 외에는 Essentials 를 이용해도 무방합니다.
- Project Online 구독을 위한 라이선스의 필요 조건은 <http://www.itfutures.co.kr/contact.html> 를 참조하여 문의주시기 바랍니다.

Office 365 Service

Project Online Essentials

Project Online Professional (P3 PLAN)

Project Online Premium (P5 PLAN)

서비스 대상

팀 구성원 (MS Project Professional 설치 라이선스 없음)

프로젝트관리자, 자원관리자,
MS Project Professional 설치 가능

포트폴리오 관리자, 이해관계자, 임원 등

Project Online Service type

Project Manager = Project Online Professional
Team member = Project Online Essentials
PMO, Portfolio Manager , CEO , CIO = Project Online Premium

Project Online Essentials

¥7,900.00 user/month

Collaborate on projects online, view and manage tasks, submit timesheets, and flag issues or risks. Requires Project Online or Project Server for ...

Office 2016 desktop & mobile apps
Not included

Office 365 services



Project Online Professional

¥33,700.00 user/month

A complete online project management solution to help keep your projects, resources, and teams organized and on track. Plan projects ...

Office 2016 desktop & mobile apps



Office 365 services



Project Online Premium

¥61,900.00 user/month

A flexible solution for project portfolio management and everyday work. Includes the Project client for people who need full project management ...

Office 2016 desktop & mobile apps




Office 365 services



Step 1: sign up for Office 365

Project Online 가입

<https://products.office.com/ko-kr/project/project-online-professional>



Project Online Professional

프로젝트, 리소스 및 팀을 체계적으로 유지하고 일정대로 진행하세요. 어디서나 쉽고 효율적으로 프로젝트를 계획하고, 상태를 추적하며, 다른 사용자와 공동 작업할 수 있습니다.


₩33,700 사용자당/월	지금 구입
또는 무료 체험	체험하기

가격에는 부가가치세가 포함되어 있지 않습니다.

Project

Step 2: get started with Project Web App

- PWA 사이트 생성.
- 언어 설정에서 한국어 등 다국어 설정



Step 3: get started with Project Pro for Office 365

- Click-to-run: Project Pro for Office 365 인터넷을 통하여 바로 실행
- 설치 미디어를 통해 설치 후 구독자 등록
- 항상 Microsoft Project 최신 버전으로 사용 가능
- 구독자 당 5대의 PC에 설치가능

소프트웨어

Office

도구 및 추가 기능

Project


비즈니스용 Skype

전화 및 태블릿

Project

Project 2016 [설치\(권장\)](#) [Office 2013의 변경 사항](#)

참고: 관리자가 첫 번째 릴리스를 사용하도록 설정했으므로 최신 Office 기능을 먼저 이용해 볼 수 있습니다. 의견이나 문제가 있으면 관리자에 문의하세요.



Project

언어: 버전: 32비트(권장) [고급](#)

Don't see the language you want? Install one of the languages in the list above and then install a [language accessory pack](#). Additional languages and language accessory packs don't count against your install limit.

Project

Step 4: Project Online 기능 사용

Project Web App Settings
Demand Management
Portfolio Management
WBS template
Etc.

The screenshot displays the Microsoft Project Web App interface. At the top, the Office 365 header shows the user 'Jeong James' and navigation options like '뉴스피드', 'SkyDrive', '사이트', and '프로젝트'. The main content area is titled '프로젝트 센터' (Project Center) and features a Gantt chart for 'Health Assessment Reporting Tool' (3-12 - 9-5). The Gantt chart shows various project tasks with their start and end dates, such as 'Payroll System Upgrade' (7-24 - 2-21) and 'Merger and Acquisition Deal Room' (2-28 - 7-9). Below the Gantt chart is a table listing project details:

프로젝트 이름 ↑	시작	마침	완료율	2013-04-14	2013-04-21	2013-04-28
Project Departments:	2012-06-29	2013-11-30	0%			
Ignite User Conference	2012-06-29	2013-11-30	0%			
Project Departments: Finance	2012-01-13	2015-05-07				
Apparel ERP Upgrade	2013-01-28	2013-08-30	99%			
Audit Tracking Solution	2013-01-21	2013-07-30	0%			
Biothermal ear heating system for helmets	2012-01-13	2014-02-05	18%			
Content Filtering Design and Implementation	2012-02-20	2012-12-14	33%			
Currency Translator Upgrade	2013-02-04	2013-07-16	0%			
Health Assessment Reporting Tool	2012-03-12	2012-09-05	61%			
Helmet with integrated sunvisor	2013-02-04	2015-05-07	0%			
Router Benchmark System Upgrade	2012-07-24	2013-01-11	5%			
Tax Checker	2013-01-14	2013-06-11	0%			
Project Departments: IT	2012-01-09	2013-10-25				
Data Exchange and Integration	2013-05-13	2013-10-25	0%			
Data Parsing Tool	2013-01-15	2013-07-09	0%			
Dynamics CRM Deployment EMEA	2012-01-09	2012-07-06	96%			
E-commerce Portal Development	2012-07-02	2013-01-16	0%			
Employee Detection Tracking System	2013-06-10	2013-02-06	0%			

Project

Getting started with Project Online

- Project Creation
- Project Workflow
- Resource Management
- Managing Control

Create new Project

- Enterprise Project Type 을 이용하여 새 프로젝트 생성



Create new Project

Project Initiation		Business Case	
Name *	<input type="text" value="Core i7 notebook nt13-a dev"/>	Problem Statement Describe the Contoso business problem that this project was created to address. The problem may be process, technology, or product/service oriented.	<input type="text" value="무게 1kg 미만으로 개발"/>
Description	<input type="text" value="Core i7 notebook nt13-a dev"/>		
Project Departments Primary Contoso Divisions	<input type="text" value="New Product Development"/> ...	Expected Benefit Brief description of the expected benefits to the Contoso business or organization.	<input type="text" value="최소무게의 노트북 탄생"/>
Proposed Start Project Requester proposed project start date.	<input type="text" value="7/2/2018"/> 📅	Proposal Costs Provide total project cost including labor, material and expense costs.	<input type="text" value="\$500,000.00"/>
Proposed Finish Project Requester proposed finish date.	<input type="text" value="9/28/2018"/> 📅	Benefits Expected cost benefits for this project.	<input type="text" value="\$5,000,000.00"/>
Program The Contoso Program to which this specific project is assigned.	<input type="text" value="Gladstone"/> ...	ROI Return on investment. Calculated as Benefits / Proposal Costs.	
Location The project location where the majority of the work is to be completed. Enter in the format of City, ST for the US. Use City, Country for other Countries.	<input type="text" value="SEOUL"/>	Proposed 'Go Live' Date Target date for this project to be placed into production.	<input type="text" value="7/2/2018"/> 📅
Owner	<input type="text" value="Adele Vance"/> Browse...		
Sponsor Contoso specific IT/Marketing Sponsor for this specific project.	<input type="text" value="Lynne Robbins"/> ...		

Project Workflow

Workflow Status

1 - Proposal

1M - Initial Business Case

2 - Selection

Current Workflow Stage: **1M - Initial Business Case**

Workflow Stage Status

A new Business Case has been created. Please complete any required information on the associated Project Detail Pages (PDPs) including the Strategic Impact for this initiative and click "Submit" when ready to submit for review.

Sections to be completed for this stage:

Pages below may require attention. Click "Next" in the ribbon above to scroll through each page or select an individual page by clicking on it below.

	Page Name	Status	Description
	Business Case	Complete	PDP to be filled in when initiating a development project in PWA which follows the Major Workflow process. This PDP will pro
	Strategic Impact	No Required Project Fields	This section captures how this Proposal impacts the Strategic Business Drivers
	Schedule	No Required Project Fields	This section captures Schedule information (like Milestones and Tasks)

Pages marked with "*" require attention

All Workflow Stages

Workflow Stage status may not show current information until the project is either Submitted or the page is Refreshed.

	Stage	State	Entry Date	Completion Date	Status Info
	Workflow Phase: 1 - Proposal				
➔	1M - Initial Business Case	In Progress (Waiting for Input)	6/21/2018 5:07 AM	6/21/2018 5:07 AM	A new Business Case has been created. Please complete any required informa
	Workflow Phase: 2 - Selection				
	2M - Steering Committee Review	Not Started			
	Workflow Phase: 3 - Planning				
	3M - Detailed Scope and Schedule	Not Started			
	4M - Baseline Schedule Review	Not Started			
	Workflow Phase: 4 - Execution				
	5M - Project Execution, Monitorin	Not Started			
	6M - Project Closure Review	Not Started			

Portfolio Management

- 프로젝트 포트폴리오 관리를 위해 전략적 영향에 대한 요인 기재
- 기재한 내용을 이용하여 프로젝트 우선순위를 설정하게 됨

Project Strategic Impact

Rate the impact of this project on the business drivers below.

Expand into new markets and segments

Expand revenue growth by penetrating new markets and expanding reach to segments of penetrated markets.

- No Rating
- None: Does not grow revenue from any markets and segments
- Low: Grows revenue from new markets and segments by up to \$500K
- Moderate: Grows revenue from new markets and segments by \$500K to \$1M
- Strong: Grows revenue from new markets and segments by \$1M to \$3M
- Extreme: Grows revenue from new markets and segments by more than \$3M

Improve customer satisfaction score

Measurably improve scores on customer satisfaction surveys through implementing standardized customer service processes, grow the number of customer service relationships, and improve the nature of each relationship.

- No Rating
- None: Does not change customer satisfaction index
- Low: Increases customer satisfaction by up to 2%
- Moderate: Increases customer satisfaction by 2% to 3%
- Strong: Increases customer satisfaction by 3% to 5%
- Extreme: Increases customer satisfaction by 5% or more

Increase market share in existing markets

Improve market share percentage or market position in existing markets.


- No Rating
- None: Has no impact on market share
- Low: Improves share in penetrated markets by less than 1%
- Moderate: Improves share in penetrated markets by 1% to 3%
- Strong: Improves share in penetrated markets by 7% to 15%
- Extreme: Improves share in penetrated markets by more than 15%

Reduce expense base


Implement standardized practices across organization to reduce expense.

- No Rating
- None: Does not reduce expense base
- Low: Reduces expense base by up to \$250K
- Moderate: Reduces expense base by \$250K to \$500K
- Strong: Reduces expense base by \$500K to \$1M
- Extreme: Reduces expense base by more than \$1M

Project Priority

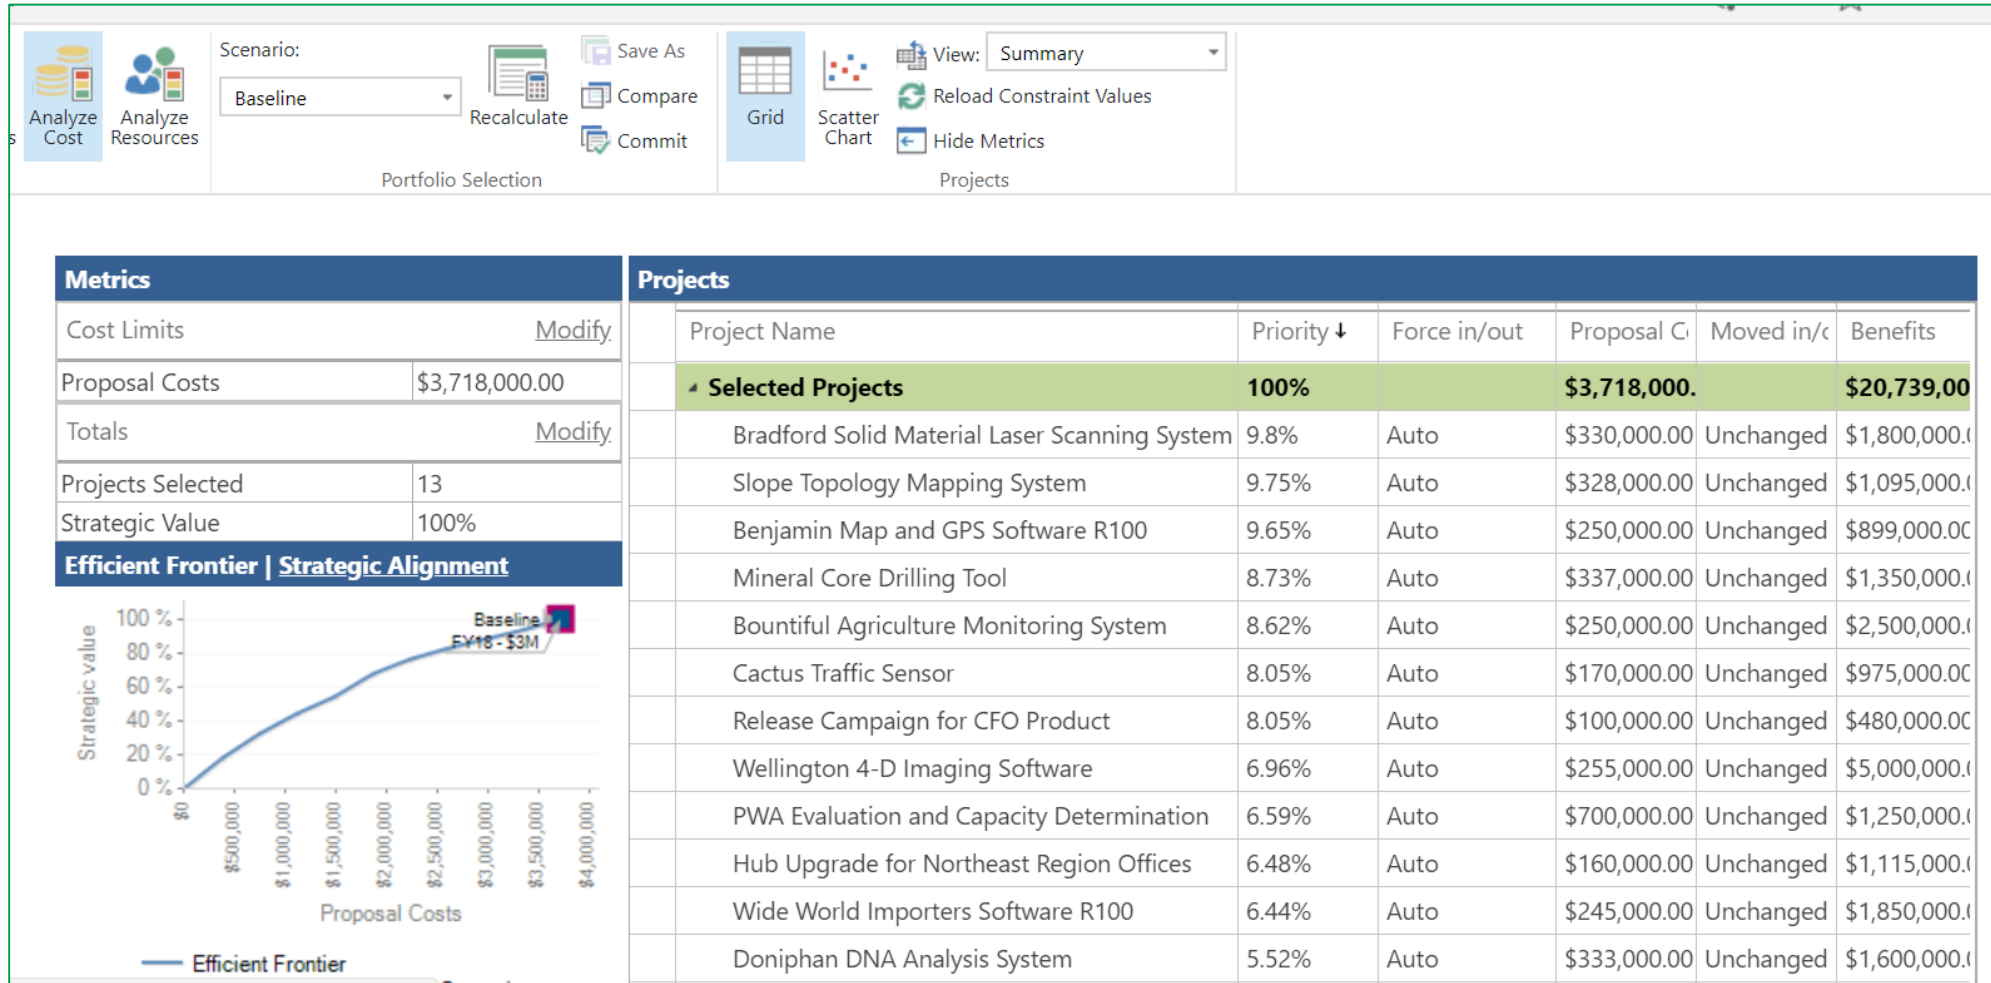

Manage Resources

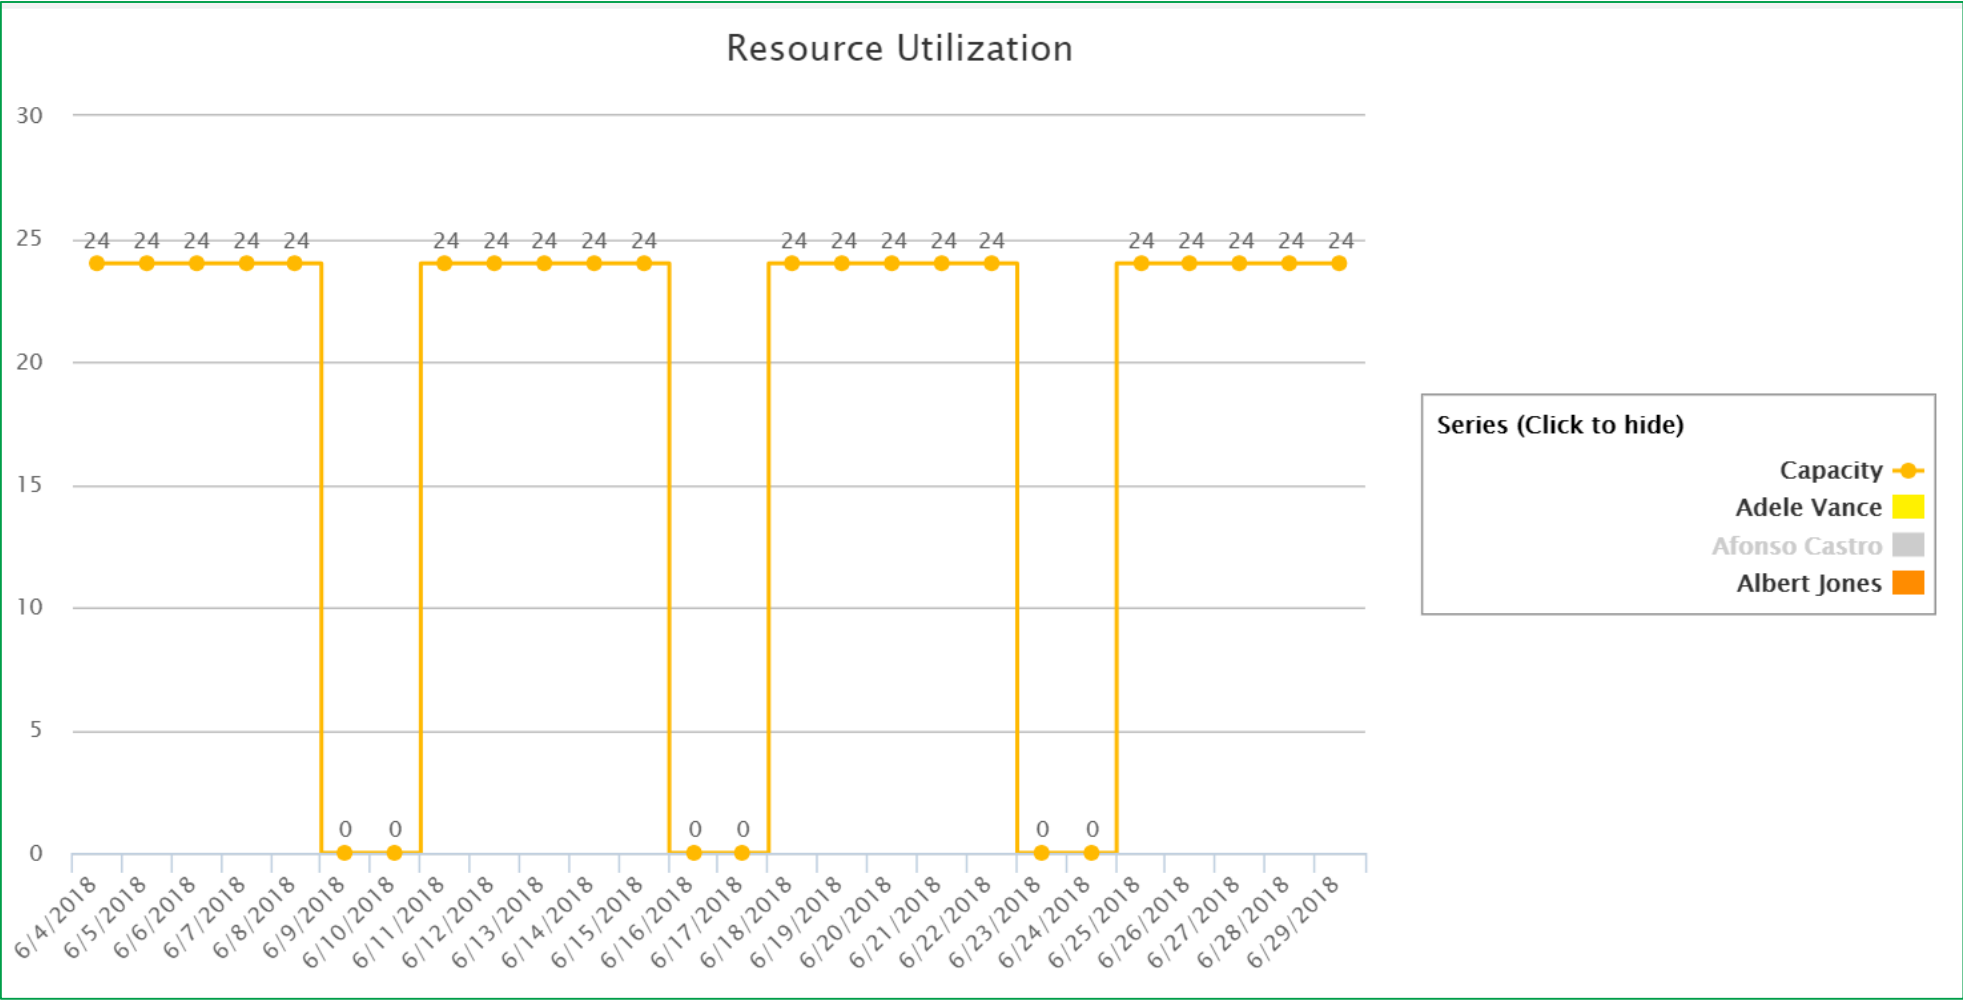

Control Project

Office 365 | Project

BROWSE PROJECT PAGE **TASK** OPTIONS

SHARE FOLLOW

Clipboard Project Editing Tasks Data Zoom

View: Tasks Summary
Filter: No Filter
Group By: No Group

Zoom In Zoom Out Scroll to Task

Project Intake
Ideas
New Proposal

My Activities
Calendar
Tasks
Manage Timesheets
Timesheet
Issues & Risks
Approvals (Tasks)
Approvals (Workflow)

Dashboards
Project Center

Daily Cleaning Activities
1/10 - 12/31

Project Start
1/2

Project Complete
12/31

ID	Mode	Task Name	Duration	Start	Finish	% Complete
1		Project Start	0d	1/2/2018	1/2/2018	100%
2		Initial Assessment	3d	1/2/2018	1/4/2018	100%
3		Perform Building Assessment	3d	1/2/2018	1/4/2018	100%
4		Review typical usage scenarios	1d	1/2/2018	1/2/2018	100%
5		Review typical customer needs	1d	1/3/2018	1/3/2018	100%
6		Identify anticipated problem points	1d	1/4/2018	1/4/2018	100%
7		Building Assessment Complete	0d	1/4/2018	1/4/2018	100%
8		Service Planning	6d	1/5/2018	1/12/2018	100%
9		Design Support Services	6d	1/5/2018	1/12/2018	100%
10		Review Customer Service Contact	3d	1/5/2018	1/9/2018	100%
11		Online support	1d	1/5/2018	1/5/2018	100%
12		Phone support	1d	1/8/2018	1/8/2018	100%
13		On-site support	1d	1/9/2018	1/9/2018	100%

1/31/2017 1/7/2018

Collaboration Project

- Issue , risk, documents management using Project Workspace

Project Web App Home EDIT LINKS Search this site

Bay Plaza

Project Summary

Steel Erection due in 147 days
41 late | 5 upcoming

Task	Start	End
Excavation	4/20/18	4/20/18
Steel Erection	7/5/18	11/15/18
Form and Pour Concrete - Floors and Roof	8/2/18	6/11/19
Masonry Work	9/27/18	9/3/19
Heating and Ventilating - AC	10/25/18	3/25/19
Elevators	10/25/18	12/20/18
Electrical	3/26/19	3/16/20
Roofing	8/6/19	10/28/19
Building Finishes	11/4/19	4/6/20
Window wall and store front closures	8/6/19	1/6/20
Plumbing	9/3/19	3/2/20
Final Clean-up	3/25/20	5/18/20

Risks

+ new item or edit this list

Current View Find an item

Title	Assigned To	Due Date
Possible additional ancient ruins may be discovered	Grady Archie	1/8/2018 12:00 AM
Unplanned City Code changes may affect the planned design and build	Grady Archie	8/23/2019 12:00 AM
Concrete Supplier may not be financially viable in the future	Grady Archie	4/19/2019 12:00 AM

Issues

+ new item or edit this list

Current View Find an item

Title	Assigned To	Due Date
Discovery of Ancient Ruins causing significant cost and time impacts	Grady Archie	1/31/2018 12:00 AM
Increased Building construction causing a concrete shortage and increased costs	Grady Archie	2/18/2019 12:00 AM
General Contractor Manager is leaving the company 4Q18	Grady Archie	11/12/2018 12:00 AM

Documents

+ New Upload Sync Share More

Current View Find a file

Name	Modified	Modified By
Welcome to PowerPoint	August 21, 2017	Lidia Holloway
Welcome to Word	August 21, 2017	Lidia Holloway
Integration Test Plan	August 21, 2017	Lidia Holloway
InternetExplorer 8	August 21, 2017	Lidia Holloway

Deliverables

+ new item or edit this list

Current View Find an item

Title	Deliverable Finish
Install store front doors and hardware	2/11/2019
Set rooftop equipment	4/5/2019
Install light fixtures - test and clean	8/23/2019
Remove debris from building and do final clean-up	10/25/2019
Obtain certificate of occupancy	12/11/2019

Project Online Reporting using Power BI

Power BI 시각화 솔루션

Power BI는 빠르게 만들고 쉽게 공유할 수 있으며, 어디서나 활용할 수 있습니다.



01

보고서 제작

Power BI Desk-Top

Power BI Desk-Top
무료 다운로드 반
응형 보고서 다양
한 시각화개체
DAX 기반 모델링



Excel

Excel
친숙한 사용자 Tool
Pivot Table 보고서
Power Pivot



02

보고서 / 대시보드 게시

Cloud Power BI

Power BI

Cloud Power BI
Pre-Packaged 기반의
편의 기능 활용 개인
화 대시보드
Realtime 대시보드



사내 구축형 Power BI

Power BI Reporting Service
보고서 포탈 정
형보고서 & KPI
모바일 보고서



03

보고서 / 대시보드 소비

모바일 전용 앱 (PowerBI 앱)

윈도우 폰 용 앱



안드로이드 폰 용 앱



iOS 용 앱



웹 포털



인터넷 브라우저

Internet Explorer



Project Online Contents Pack

<https://docs.microsoft.com/ko-kr/power-bi/service-connect-to-project-online>

AppSource | Apps for Power BI

< Apps

Microsoft Project Online

Microsoft

Overview [Reviews](#)

Unlock insight from Project Online to help manage projects, portfolios and resources.

Import and analyze data from Project Online in Power BI. The content pack is designed to help you quickly connect to your Project Online tenant in Office 365 and download a variety of data to visually explore and monitor all the key aspects of your project, portfolios and resources through 13 visually rich report pages.

GET IT NOW

Products
[Power BI apps](#)

Publisher
Microsoft

Acquire Using
Work or school account

Version
1.8

Updated
1/17/2018

Categories
[Analytics](#)

Support
[Help](#)

Legal
[Privacy Policy](#)

PORTFOLIO DASHBOARD

PROJECT COUNT: 58
PROJECT COST: \$19M
COST VARIANCE: \$7.27M
PROJECT WORK: 275K
WORK VARIANCE: 114.31K
ACTIVE RISKS: 18
ACTIVE ISSUES: 14

PROJECT NAME	PROJECT OWNER	START DATE	FINISH DATE	COST	EST.	PROG. HEALTH	CONFIDENCE	% COMPLETE
Adventures in Color Building Maintenance	Luke Langer	1/2/2018	12/31/2018	\$383,700		●	●	85%
APAC Network Expansion	Luke Langer	1/1/2019	10/31/2019	\$6,800		●	●	0%
Big Trees	Luke Langer	6/20/2017	1/2/2019	\$1,380,852		●	●	4%
Inf. Analytics Analysis Tool	Ben Madson	8/6/2017	10/31/2017	\$74,800		●	●	0%
Integrate Map and GIS Software 4108	Luke Langer	1/1/2019	1/2/2020	\$209,500		●	●	0%
Introduce the Warning System	Luke Langer	1/6/2018	2/1/2019	\$340,100		●	●	89%
Map from the Office Right towards System Integration	Luke Langer	4/16/2019	10/31/2019	\$116,800		●	●	0%
SmartFarm Agriculture Monitoring System	Luke Langer	2/1/2019	1/26/2020	\$230,700		●	●	0%
SmartFarm Field Manual User Training System	Luke Langer	5/16/2019	1/14/2020	\$199,800		●	●	0%
Carfax Traffic System	Luke Langer	1/1/2019	12/31/2019	\$158,800		●	●	0%
Cloud-based Journal Tracking System	Chris Archer	1/1/2019	1/1/2020	\$199,800		●	●	0%
Cloud-based Survey System - Marketing Research	Luke Langer	4/16/2019	10/31/2019	\$166,800		●	●	32%



★ Favorites >

🕒 Recent >

🗃 Apps

👥 Shared with me

📄 Workspaces >

👤 My Workspace ▾

↗ Get Data



Connect to Microsoft Project Online

PWA Site URL

Project Web App (PWA) URL for your organization should look like `https://contoso.sharepoint.com/sites/pwa`. Just replace 'contoso' with your tenant name and 'pwa' with your Project Web App name. If you have your own domain, replace the entire URL.

PWA Site Language

Type '1' for English, '2' for French, '3' for German, '4' for Portuguese (Brazil), '5' for Portuguese (Portugal) and '6' for Spanish.

Need help connecting? [Learn more](#)

Next







Cancel

- Favorites
- Recent
- Apps
- Shared with me
- Workspaces
- My Workspace
- DASHBOARDS
 - Microsoft Project Online
- REPORTS
 - Microsoft Project Online
 - Microsoft Project Online
- WORKBOOKS
 - You have no workbooks
- DATASETS
 - Microsoft Project Online
- Get Data

Ask a question about your data

MILESTONES UPCOMING IN THE NEXT 30 DAYS

PROJECT	MILESTONE
Employee Reporting Portal Upgrade for Contoso EU Offices	Training Materials Complete
Bay Plaza	Foundations Complete

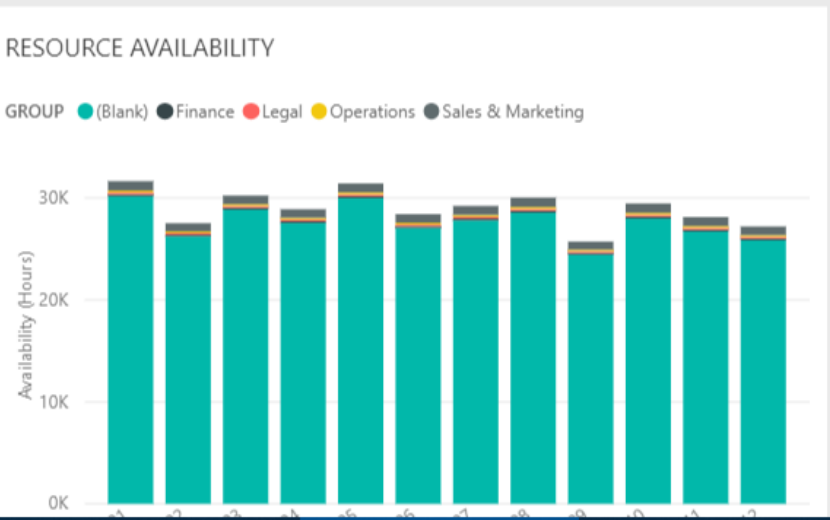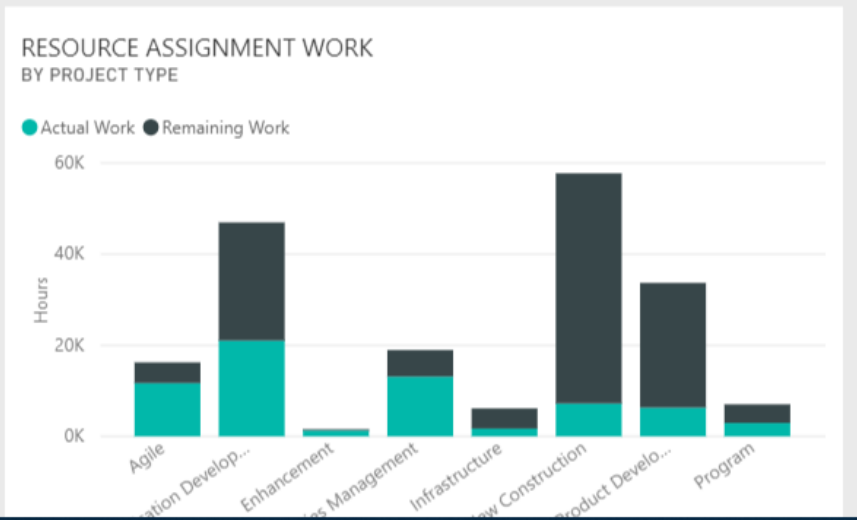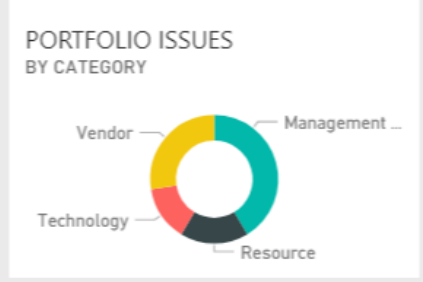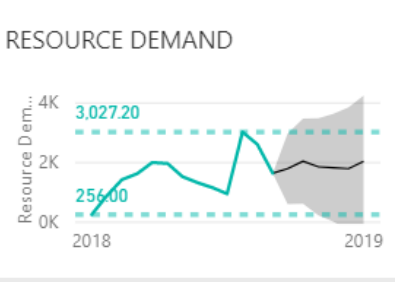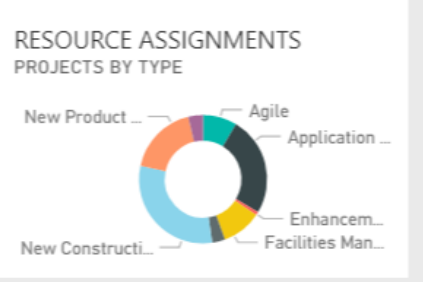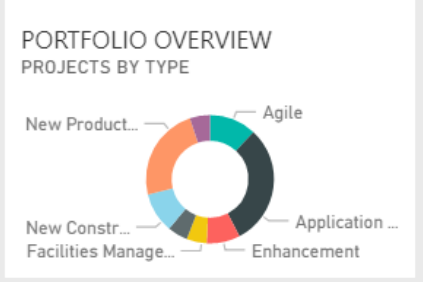

PORTFOLIO DASHBOARD

DEPARTMENT

All

PROJECT TYPE

All

PROJECT OWNER

All

GOVERNANCE PHASE

All

PROJECT COUNT

61

PROJECT COST

19M

LOCAL CURRENCY

COST VARIANCE

7.28M

LOCAL CURRENCY

PROJECT WORK

275K

HOURS

WORK VARIANCE

114.51K


HOURS

RISKS COUNT


34

ISSUES COUNT

PROJECTS BY GOVERNANCE PHASE

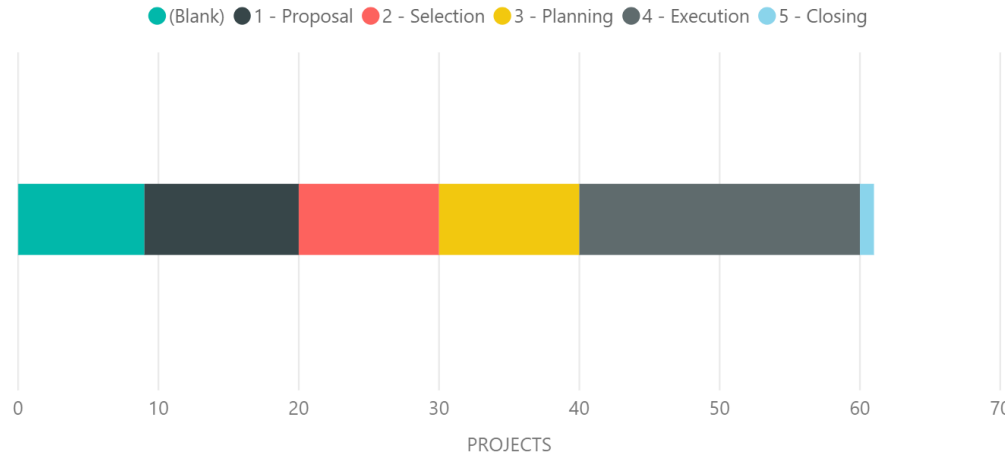

PROJECTS BY TYPE

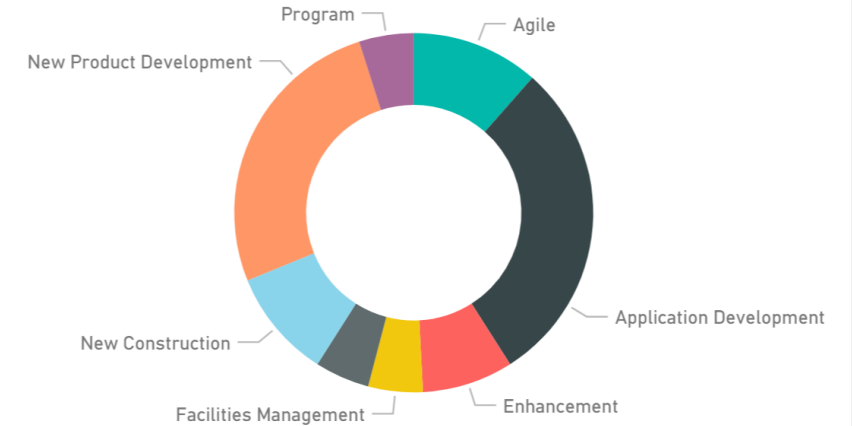

PROJECT NAME	PROJECT OWNER	START DATE	FINISH DATE	COST	COST HEALTH	WORK HEALTH	SCHEDULE HEALTH	% COMPLETE
Core i7 notebook nt13-a dev	Adele Vance	21-Jun-18	22-Jun-18	0	●	●	●	0 %
Electronic Asset Tracking Update	Lidia Holloway	18-Oct-17	22-Jan-19	0	●	●	●	0 %
sample project A	Jeong James	21-Jun-18	17-Jul-18	6,760	●	●	●	0 %
Online Payment Feature for E-commerce Site	Christie Cline	17-Sep-18	16-Nov-18	20,865	●	●	●	27 %
AdventureWorks Cycles Building Maintenance	Lidia Holloway	02-Jan-18	31-Dec-18	563,180	●	●	●	66 %
APAC Network Expansion	Lidia Holloway	01-Oct-18	23-Oct-18	8,060	●	●	●	0 %
Bay Plaza	Lidia Holloway	05-Jun-17	02-Jul-20	1,690,052	●	●	●	4 %
Bell Linguistics Analysis Tool	Adele Vance	04-Aug-17	02-Oct-17	74,360	●	●	●	0 %
Benjamin Map and GPS Software R100	Lidia Holloway	21-Jan-19	27-Jan-20	229,500	●	●	●	0 %
Biothermal Ear Warming System	Isaiah Langer	08-Jan-18	01-Feb-19	345,181	●	●	●	69 %
Bountiful Agriculture Monitoring System	Isaiah Langer	11-Mar-19	29-Jul-20	229,720	●	●	●	0 %

발표자 소개

ITFutures

Project

아이티퓨처스 사업영역



마이크로소프트의 Project 전문 솔루션파트너로서 지난 11여년간 다수의 기업 및 공공연구소에서 프로젝트 관리 솔루션 구축 및 컨설팅을 수행하고 있습니다.



프로젝트 관리 솔루션

PROJECT POINT 2016

- **Project Point (프로젝트 관리 솔루션 - 자체 개발)**
 - 프로젝트 팀이 작업, 변경요청, 이슈, 리스크, 산출물 등을 확인하고 프로젝트 상태 및 자원 할당에 대한 실시간 보고를 통해 팀이 업무를 원활하게 진행할 수 있도록 지원
 - 모바일로 팀과 연결된 상태로 유지하고 프로젝트를 제어할 수 있는 도구를 사용하여 언제 어디서나 관리
 - 조직이 의도된 비즈니스 가치를 달성할 수 있도록 직관적인 컨트롤과 유연한 팀 도구를 사용하여 간편하게 프로젝트를 계획 및 관리
- **Microsoft Project Server (마이크로소프트 프로젝트 관리 솔루션)**
 - 유연한 온-프레미스 및 클라우드 기반 솔루션
 - 간편한 운영 및 관리
 - 공동 작업 및 커뮤니케이션
 - 모든 작업 관리 : 작업, 제안, 리소스, 일정, 프로그램 등 관리
 - 고급 포트폴리오 관리 : 재무관리, 포트폴리오 분석 및 선택
 - 데이터 기반 결정 : 문제점 및 위험 관리, 보고 및 BI
 - Office 365를 이용한 확장성











프로젝트 관리 컨설팅




- **현재 수준 진단 컨설팅**
 - 대상 기업의 PMO 및 현업 사용자 그룹 (PM, PL, 연구원)과 인터뷰 진행
 - 인터뷰를 바탕으로 현재 프로젝트 관리 수준 파악 및 개선안 도출
- **PMO 구성 컨설팅**
 - 프로젝트지원조직(Project Management Office)PMO 구성에 대한 가이드
 - 타사 사례 분석, 타사의 프로젝트 관리 사례를 분석하여 벤치마킹 보고서 작성
- **WBS 표준 프로세스 컨설팅**
 - 프로젝트관리 시스템 구축을 위한 가장 중요한 부분으로서 WBS 템플릿의 기준을 설정함.
 - 표준적인 WBS의 구조 체계를 선정
- **Task 산출물 체계 컨설팅**
 - 각 템플릿의 주요 단계에서 나와야 하는 산출물의 종류를 설정하여 주요 프로세스의 확인 및 검증 체계를 수립

주요 수행실적

고객사명	프로젝트명
 LG이노텍	<ul style="list-style-type: none"> • R&D 연구 프로젝트 관리
 HYUNDAI MOBIS	<ul style="list-style-type: none"> • 신규거점패키지 관리 시스템 구축
 SAMSUNG 삼성전자	<ul style="list-style-type: none"> • 사업부 PLM : 상품개발 라이프사이클 관리 • 전사 S/W프로젝트 관리 : S/W 프로젝트 일정, 자원, 개발자 관리 • LSI 사업부 신제품 연구개발 프로젝트 관리 • 통신연구소 R&D 연구개발 프로젝트 관리 • TSST 제품 개발 프로젝트 관리
 DRB 동일	<ul style="list-style-type: none"> • 동일고무벨트 PI(Process Innovation) 진행관리
 VOLVO	<ul style="list-style-type: none"> • 볼보건설기계코리아 전사 R&D 관리 시스템 구축
 ETRI 한국전자통신연구원 Electronics and Telecommunications Research Institute	<ul style="list-style-type: none"> • EPM 및 CCPM 기반의 대표 프로젝트 관리
 KAERI 한국원자력연구원 Korea Atomic Energy Research Institute	<ul style="list-style-type: none"> • 고속로기술개발부 프로젝트 관리 시스템
 HYUNDAI KEFICO	<ul style="list-style-type: none"> • CCMI Level 3 기반의 프로젝트관리
 HYUNDAI AUTRON	<ul style="list-style-type: none"> • 프로젝트 관리 시스템
 DongHwa Entec	<ul style="list-style-type: none"> • 제품개발일정관리




**IT FUTURES**

Enterprise Project Management Partner

프로젝트 관리 컨설팅 / 솔루션 전문기업

아이티퓨처스

아이티퓨처스는 마이크로소프트사의 EPM 전문 파트너 기업입니다.
연락처 : 정수현 대표컨설턴트(james@itfutures.co.kr) , 010-4545-6822



Microsoft
